LCTCS

PROGRAM UPDATE

January 5, 2020

ACT 391 | ACT 360 I SOWELA DISASTER RECOVERY | OTHER

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

ACT 391 | ACT 360
STATEWIDE FACILITIES IMPROVEMENT PROGRAM

LCTCS ACT 391

PROJECT UPDATES

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

NUNEZ COMMUNITY COLLEGE

CLASSROOM BUILDING A & BREEZEWAY

PROJECT:	ACT 391 PROJECT FUNDS
LOCATION:	Chalmette
REMAINING ACT 391 FUNDS:	$178,244

PROJECT STATUS:

- Coordinating with the Campus to expend remaining project funds on reimbursements.
- Hot Water Heater contract awarded to Boasso Construction for the base bid amount of $134,500.
- Work to begin on January 11th, 2021.
- Remaining funds allocated to parking lot and landscaping installation.

LCTCS ACT 360 PHASE I

CLOSE-OUT & WARRANTY

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

CENTRAL LOUISIANA TECHNICAL CC

ALEXANDRIA CAMPUS (DOWNTOWN CAMPUS)

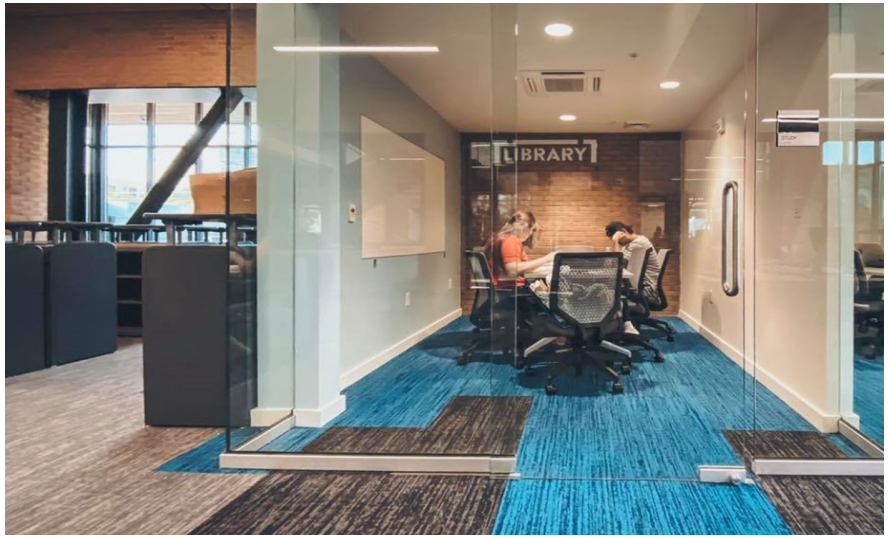

PROJECT:	Alexandria Campus
LOCATION:	Alexandria
BUILDING SIZE:	50,000 sq. ft.
ACT 360 FUNDS:	$19,000,000
12% MATCH (CASH):	$2,600,000
OVERALL FUNDING:	$21,600,000
CONSTRUCTION COST:	$16,874,773
ARCHITECT:	BHB | ABW, Joint Venture
GENERAL CONTRACTOR:	Ratcliff Construction

PROJECT STATUS:

- **Cons. Costs for Downtown Campus: $10,438,888**
- Coordinating with the Campus to expend remaining project funds on reimbursements.

CENTRAL LOUISIANA TECHNICAL CC

ALEXANDRIA CAMPUS (RIVERFRONT CAMPUS)

PROJECT:	Alexandria Campus
LOCATION:	Alexandria
BUILDING SIZE:	23,000 sq. ft.
ACT 360 FUNDS:	$19,000,000
12% MATCH (CASH):	$2,600,000
OVERALL FUNDING:	$21,600,000
CONSTRUCTION COST:	$16,874,773
ARCHITECT:	BHB | ABW, Joint Venture
GENERAL CONTRACTOR:	Ratcliff Construction

PROJECT STATUS:

- **Cons. Costs for Riverfront Campus: $6,435,885**
- Coordinating with the Campus to expend remaining project funds on reimbursements.

LCTCS ACT 360 PHASE II

CLOSE-OUT & WARRANTY

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

BATON ROUGE COMMUNITY COLLEGE

ACADIAN CAMPUS

PROJECT:	Acadian Campus
LOCATION:	Baton Rouge
BUILDING SIZE:	130,000 sq. ft.
ACT 360 FUNDS:	$8,780,000
12% MATCH (CASH):	$949,999
OVERALL FUNDING:	$9,729,999
CONSTRUCTION COST:	$6,744,933
ARCHITECT:	Coleman Partners
GENERAL CONTRACTOR:	Guy Hopkins Construction

PROJECT STATUS:

- Coordinating with the Campus to expend remaining project funds on reimbursements.

LOUISIANA DELTA COMMUNITY COLLEGE

MONROE CAMPUS

PROJECT:	Monroe Campus
LOCATION:	Monroe
BUILDING SIZE:	22,000 sq. ft.
ACT 360 FUNDS:	$7,200,000
12% MATCH (CASH):	$1,000,000
OVERALL FUNDING:	$8,200,000
CONSTRUCTION COST:	$6,778,982
ARCHITECT:	Architecture +
GENERAL CONTRACTOR:	Boggs & Poole Contracting

PROJECT STATUS:

- Coordinating with the Campus to expend remaining project funds.

LOUISIANA DELTA COMMUNITY COLLEGE

TALLULAH CAMPUS

PROJECT:	Tallulah Campus
LOCATION:	Tallulah
BUILDING SIZE:	42,479 sq. ft.
ACT 360 FUNDS:	$2,500,000
12% MATCH (CASH):	$346,651
OVERALL FUNDING:	$2,846,651
CONSTRUCTION COST:	$2,040,221
ARCHITECT:	TBA Studio
GENERAL CONTRACTOR:	Don M Barron Contractor

PROJECT STATUS:

- LCTCS Facilities Corporation has approved transfer of remaining ACT 360 funds from Tallulah project to Ruston project.

NORTHSHORE TECHNICAL COMMUNITY COLLEGE

LIVINGSTON CAMPUS

PROJECT:	Livingston Campus
LOCATION:	Walker
BUILDING SIZE:	14,000 sq. ft.
ACT 360 FUNDS:	$5,130,000
12% MATCH (CASH):	$700,000
OVERALL FUNDING:	$5,830,000
CONSTRUCTION COST:	$4,474,406
ARCHITECT:	Holly Smith Architects
GENERAL CONTRACTOR:	Cangelosi Ward Contractors

PROJECT STATUS:

- Remaining project funds expended on reimbursement for pathway to Literacy Center.

LCTCS ACT 360 PHASE III

DESIGN & CONSTURCTION

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

DELGADO COMMUNITY COLLEGE

NEW NURSING AND ALLIED HEALTH BUILDING

PROJECT:	Nursing and Allied Health
LOCATION:	Orleans
BUILDING SIZE:	TBD
ACT 360 FUNDS:	$34,000,000
12% MATCH (TBD):	$4,636,363
OVERALL FUNDING:	$38,636,363
CONSTRUCTION BUDGET:	TBD
ARCHITECT:	Manning Architects | Mackey Mitchel, A Joint Venture
GENERAL CONTRACTOR:	The Lemoine Company

PROJECT STATUS:

- Meeting with Design Team, CMAR Contractor, and Owner scheduled for Tuesday, January 5th.
- Site of new building has been selected at corner of Orleans Avenue and City Park Avenue.

DELGADO COMMUNITY COLLEGE

CENTER FOR HOSPITALITY AND CULINARY SERVICES

PROJECT:	Nursing and Culinary
LOCATION:	Orleans
BUILDING SIZE:	20,000 sq. ft. (ESTIMATE)
ACT 360 FUNDS:	$9,000,000
12% MATCH (TBD):	$1,227,272
OVERALL FUNDING:	$10,227,272
CONSTRUCTION BUDGET:	$6,00,000 (ESTIMATE)
ARCHITECT:	Manning Architects | Mackey Mitchell, A Joint Venture
GENERAL CONTRACTOR:	TBD

PROJECT STATUS:

- Coordinating with Campus to finalize Program.
- Site selection at City Park Campus still in progress.

DELGADO COMMUNITY COLLEGE

ADVANCED TECHNOLOGY CENTER

PROJECT:	Advanced Technology Center
LOCATION:	Orleans
BUILDING SIZE:	32,660 sq. ft.
ACT 360 FUNDS:	$12,000,000
12% MATCH (CASH):	$1,636,365
OVERALL FUNDING:	$13,636,365
CONSTRUCTION COSTS:	$9,711,079
ARCHITECT:	Holly & Smith Architects, APAC
GENERAL CONTRACTOR:	MAPP, LLC

PROJECT STATUS:

- Construction: 74% Complete
- Contractor completing exterior glass and glazing while starting to prepare for the metal panels.
- Installation of ceiling grid on the 2nd floor ongoing.
- Painting of walls on 1st floor nearing completion ahead of ceiling install.
- Ceramic Tile is complete at all restroom.
- Monument stair has been set in the lobby.

DELGADO COMMUNITY COLLEGE

ADVANCED TECHNOLOGY CENTER

DELGADO COMMUNITY COLLEGE

ADVANCED TECHNOLOGY CENTER

DELGADO COMMUNITY COLLEGE

ADVANCED TECHNOLOGY CENTER

DELGADO COMMUNITY COLLEGE

ADVANCED TECHNOLOGY CENTER

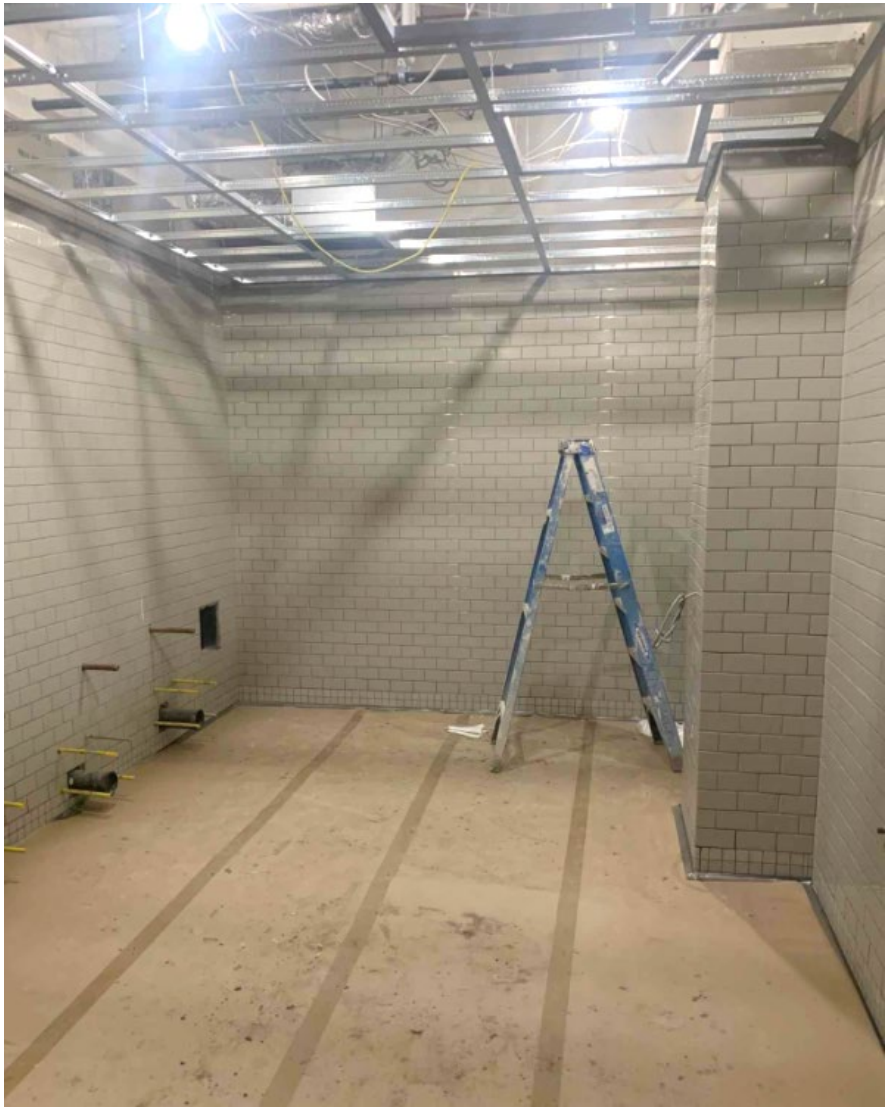

LOUISIANA DELTA COMMUNITY COLLEGE

RUSTON CAMPUS

PROJECT:	Ruston Campus
LOCATION:	Ruston
BUILDING SIZE:	30,775 sq. ft.
ACT 360 FUNDS:	$8,100,000
12% MATCH (CASH):	$1,104,546
OVERALL FUNDING:	$9,204,546
CONSTRUCTION AMOUNT:	$7,343,556
ARCHITECT:	TBA Studio
GENERAL CONTRACTOR:	Ratcliff Construction

PROJECT STATUS:

- Project to be constructed on existing campus location.
- Contractor working on pricing on finalized Construction Documents.
- Working to begin any activity on site.

LOUISIANA DELTA COMMUNITY COLLEGE

RUSTON CAMPUS

LOUISIANA DELTA COMMUNITY COLLEGE

RUSTON CAMPUS

SOWELA TECHNICAL COMMUNITY COLLEGE

CULINARY, GAMING, AND HOSPITALITY BUILDING

PROJECT:	Culinary, Gaming, and Hospitality Building
LOCATION:	Lake Charles
BUILDING SIZE:	28,000 sq. ft.
ACT 360 FUNDS:	$9,000,000
12% MATCH (CASH):	$1,227,272
OVERALL FUNDING:	$10,227,272
CONSTRUCTION BUDGET:	$8,543,266
ARCHITECT:	Champeaux Evans Hotard
GENERAL CONTRACTOR:	Pat Williams Construction

PROJECT STATUS:

- Construction: 8% Complete
- Drill shaft pours complete.
- Contractor is scheduled to pour slab this week.
- Sewage relocation complete; paperwork on sewage relocation reimbursement in progress.
- Working with City on Easement agreement for access and service for Sewer Lift Station.

SOWELA TECHNICAL COMMUNITY COLLEGE

CULINARY, GAMING, AND HOSPITALITY BUILDING

LCTCS ACT 360 PHASE IV

DESIGN UPDATES

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

DELGADO COMMUNITY COLLEGE

WORKFORCE DEVELOPMENT BUILDING

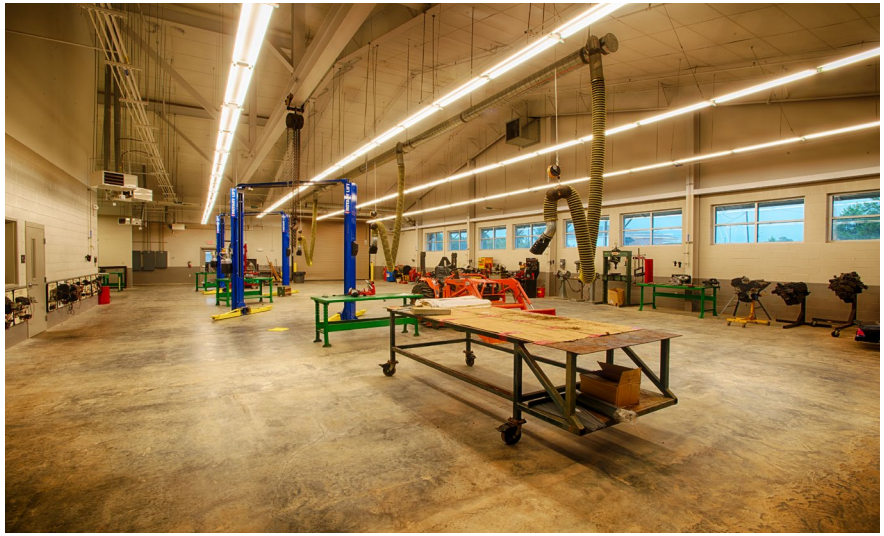

PROJECT:	Workforce Development Building
LOCATION:	Orleans
BUILDING SIZE:	20,000 sq. ft. (ESTIMATE)
ACT 360 FUNDS:	$7,200,000
12% MATCH (CASH):	$981,818
OVERALL FUNDING:	$8,181,818
CONSTRUCTION BUDGET:	$6,000,000 (ESTIMATE)
ARCHITECT:	Manning Architects | Mackey Mitchel, A Joint Venture
GENERAL CONTRACTOR:	TBD

PROJECT STATUS:

- Coordinating with Campus to finalize Program.
- Site selection at City Park Campus is in progress.

FLETCHER TECHNICAL COMMUNITY COLLEGE

NEW WORKFORCE TRAINING BUILDING

PROJECT:	Workforce Training Building
LOCATION:	Schriever
BUILDING SIZE:	25,271 sq. ft. (ESTIMATE)
ACT 360 FUNDS:	$4,500,000
12% MATCH (CASH):	$613,636
OVERALL FUNDING:	$7,714,695
CONSTRUCTION BUDGET:	$6,360,000 (ESTIMATE)
ARCHITECT:	Weimer Gros Flores, LLC
GENERAL CONTRACTOR:	TBD

PROJECT STATUS:

- Design Development Submittal due on January 4th, 2021.
- Design Team delayed on submittal, working on design schedule.

FLETCHER TECHNICAL COMMUNITY COLLEGE

NEW WORKFORCE TRAINING BUILDING

FLETCHER TECHNICAL COMMUNITY COLLEGE

NEW WORKFORCE TRAINING BUILDING

NUNEZ COMMUNITY COLLEGE

STUDENT TESTING & CAREER COUNSELING CENTER

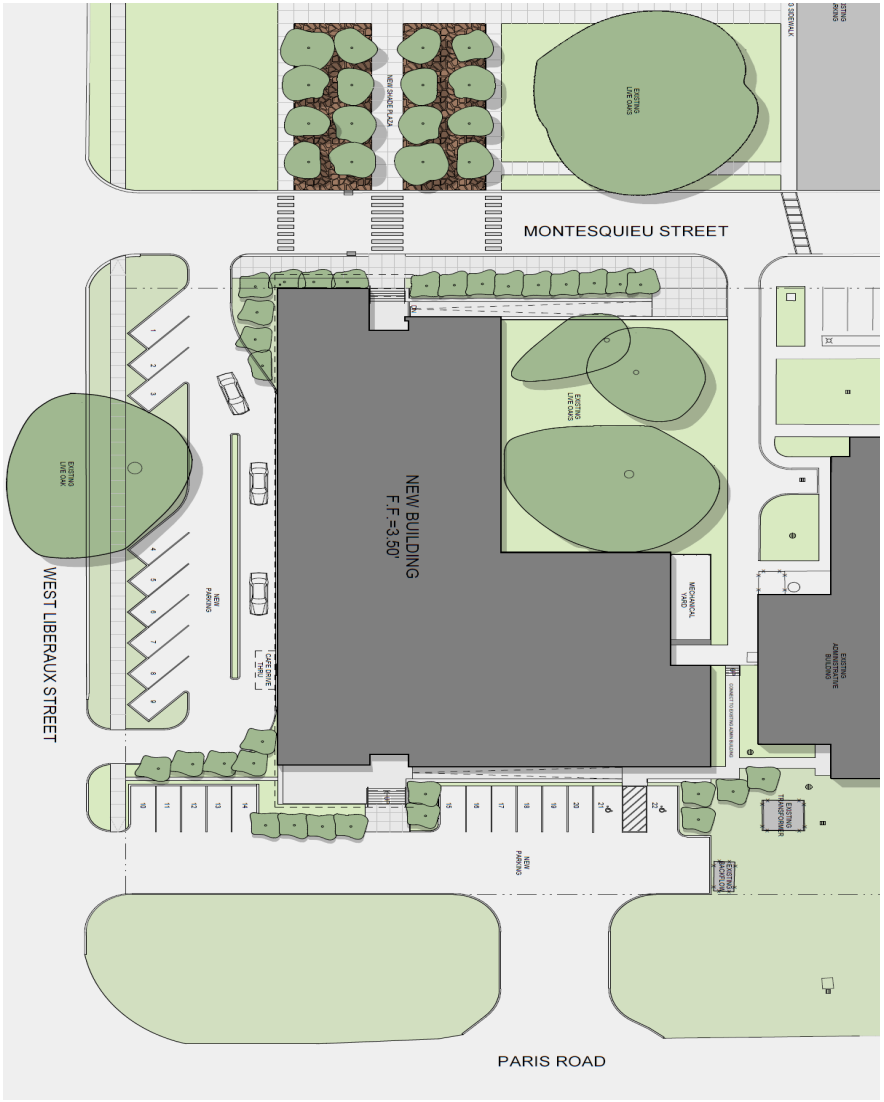

PROJECT:	Testing and Career Center
LOCATION:	Chalmette
BUILDING SIZE:	18,163 sq. ft. (ESTIMATE)
ACT 360 FUNDS:	$6,480,000
12% MATCH (LAND):	$883,636
OVERALL FUNDING:	$7,363,636
CONSTRUCTION BUDGET:	$5,000,000 (ESTIMATE)
ARCHITECT:	Holly & Smith Architects, APAC
GENERAL CONTRACTOR:	TBD

PROJECT STATUS:

- 50% CD Submittal submitted on December 31st, 2021.
- Submittal under review by Owner and Program Manager.
- FF&E dealer has been selected by Owner.

NUNEZ COMMUNITY COLLEGE

STUDENT TESTING & CAREER COUNSELING CENTER

West Perspective

NUNEZ COMMUNITY COLLEGE

STUDENT TESTING & CAREER COUNSELING CENTER

East Perspective

NUNEZ COMMUNITY COLLEGE

STUDENT TESTING & CAREER COUNSELING CENTER

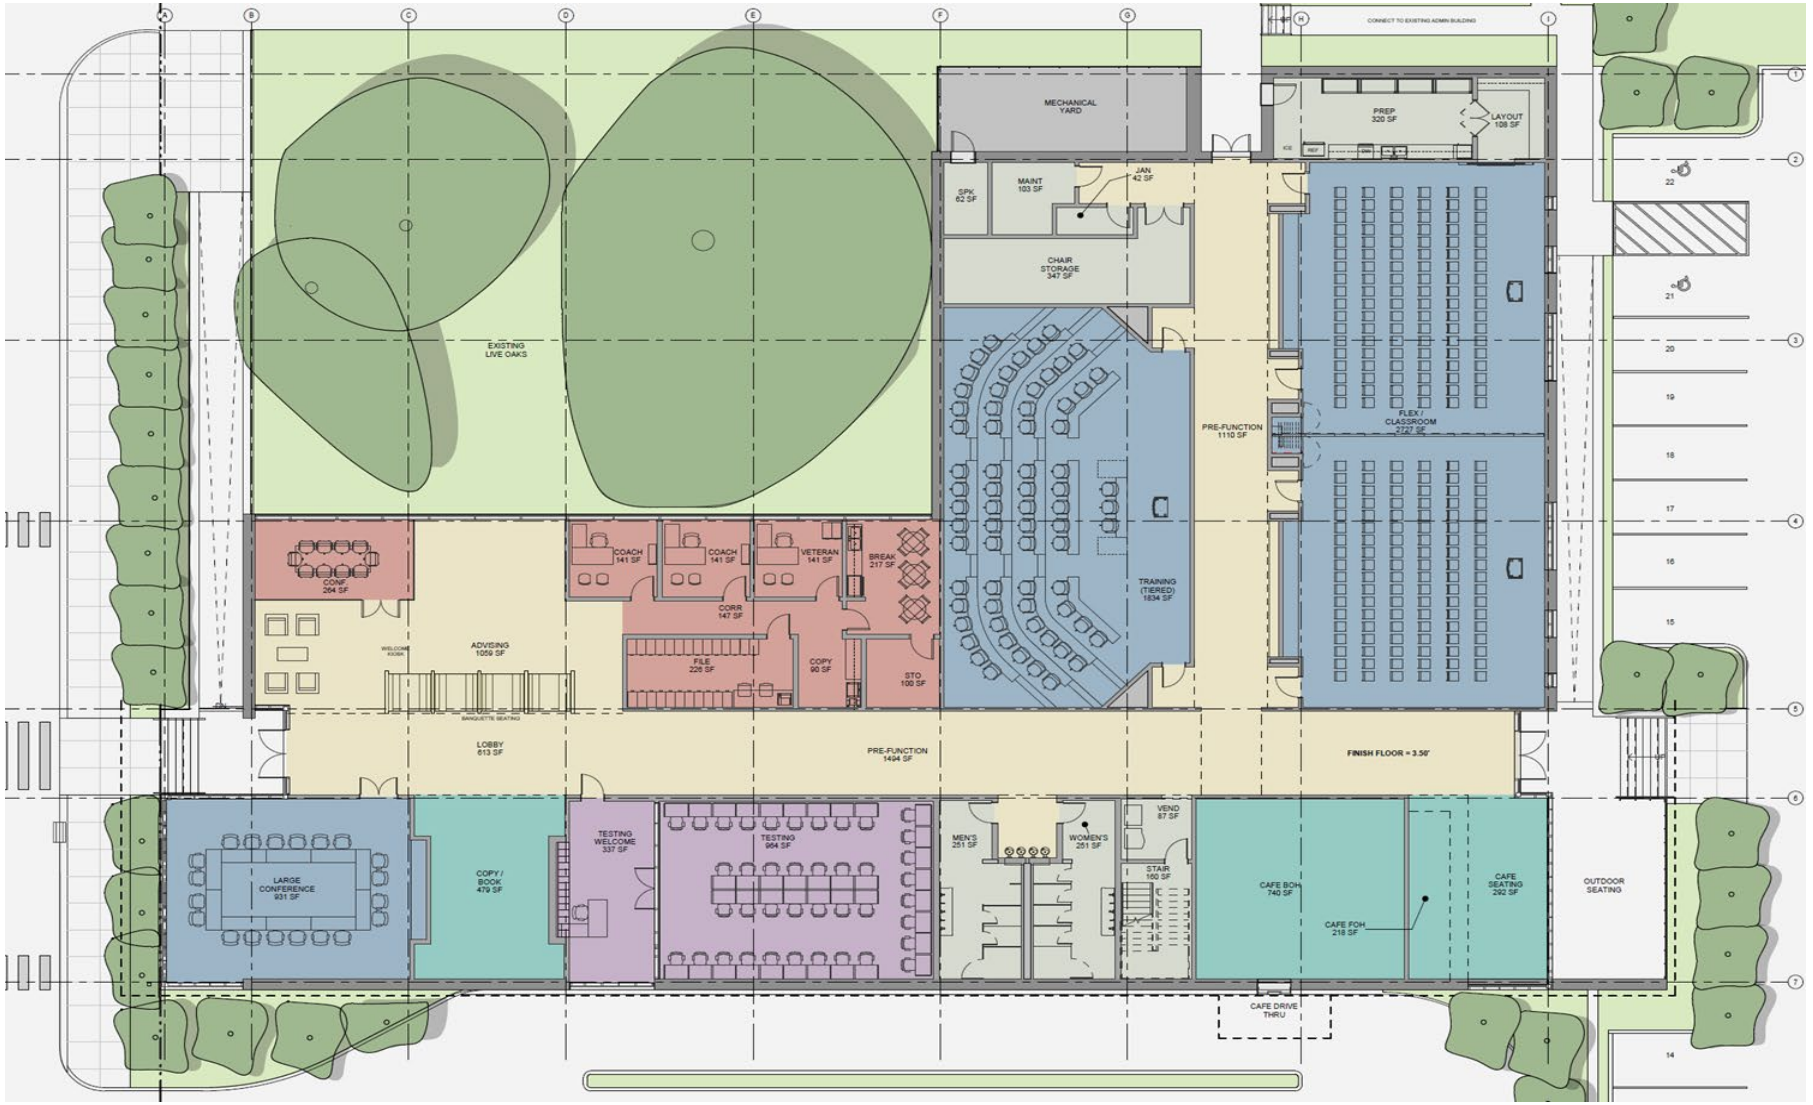

ACT 360 SMALL BUSINESS PROGRAM

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

ACT 360 SMALL BUSINESS PROGRAM

UPDATES AND OUTREACH

ACT 360 SMALL AND DISADVANTAGED BUSINESS PARTICIPATION – ACTIVE PROJECTS

ACT 360 PROJECT	GOAL	ACTUAL PARTICIPATION	IN STATE PARTICIPATION
DCC Culinary & Hospitality	25.00%	DESIGN	DESIGN
DCC Main Campus	25.00%	DESIGN	DESIGN
DCC Nursing & Allied Health	25.00%	PLANNING	PLANNING
DCC Westbank	25.00%	11.95%	98.73%
LE Fletcher Workforce	10.00%	DESIGN	DESIGN
*LDCC Ruston	3.00%	85.32%	100%
NUNEZ Testing Center	25.00%	DESIGN	DESIGN
*SOWELA Gaming & Hospitality	20.00%	1.15%	100%

**DESIGN CONTRACTS ONLY*

SBD participation in ACT 360 completed projects is **$26,871,926 - 18.52%**.
Fourteen (14) of the eighteen (18) Prime Contractors met or exceeded the SDBE goals.
In addition, **$137,269,156 - 95%** was spent with Louisiana Prime and Subcontractors.

ACT 360 SMALL BUSINESS PROGRAM

UPDATES AND OUTREACH

In partnership with the LCTCS Facilities Corporation, CSRS and Charbonnet & Associates have recently completed a series of statewide meetings regarding the LCTCS Small Business Program and contracting opportunities for the ACT 360 Facilities Improvement Program

DELGADO COMMUNITY COLLEGE, CITY PARK CAMPUS
NEW ORLEANS, LA, MARCH 11, 2019

LCTCS

SOWELA DISASTER
PROJECT UPDATES

ACT 391 | ACT 360 I SOWELA DISASTER RECOVERY | OTHER

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

SOWELA TECHNICAL COMMUNITY COLLEGE

DISASTER RECOVERY – PHASE I

PROJECT:	Disaster Recovery – Phase I
LOCATION:	Lake Charles
BID AMOUNT:	$3,800,000

BUILDINGS IN PHASE I:

- Gerstner Building
- Nursing & Allied Health Building
- Phillip 66 Process Technology Building
- Regional Training Center
- Sycamore Student Center
- Transportation Technology Building

PROJECT STATUS:

- Phase I under construction and will be completed in separate phases.
- Arkel Constructors and Roofing Solutions are onsite working and progressing.

SOWELA TECHNICAL COMMUNITY COLLEGE

DISASTER RECOVERY – PHASE I

SOWELA TECHNICAL COMMUNITY COLLEGE

DISASTER RECOVERY – PHASE I

SOWELA TECHNICAL COMMUNITY COLLEGE

DISASTER RECOVERY – PHASE II

PROJECT:	Disaster Recovery – Phase II
LOCATION:	Lake Charles
BID AMOUNT:	TBD

BUILDINGS IN PHASE II:

- Calcasieu Building
- Charleston Building
- Chennault Building
- Cypress Building
- Magnolia Building
- Pelican Building

PROJECT STATUS:

- Project to being once funding has been released.
- Phase II bid packages nearing completion.
- Advertisements for bid anticipated to begin on January 20th, 2021 per FP&C.
- Bid date anticipated to be on January 28th, 2021 per FP&C.
- Scope alignment with Office of Risk Management ongoing.

SOWELA TECHNICAL COMMUNITY COLLEGE

DISASTER RECOVERY – PHASE III

PROJECT:	Disaster Recovery – Phase III
LOCATION:	Lake Charles
BID AMOUNT:	TBD

BUILDING IN PHASE III:

- Arts & Humanities Building

PROJECT STATUS:

- Project to begin once funding has released.
- Arkel Constructors selected as Construction Manager at Risk (CMAR) Contractor.
- Site visit scheduled with Owner and CMAR Contractor on Tuesday, December 22nd.
- Pre-construction Services have started and Contractor is pricing demolition package.

OTHER PROJECTS

PROJECT UPDATES

ACT 391 | ACT 360 I SOWELA DISASTER RECOVERY | OTHER

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

DELGADO COMMUNITY COLLEGE

BASEBALL FIELDHOUSE

PROJECT:	Baseball Fieldhouse
LOCATION:	Orleans
CONSTRUCTION BUDGET:	$1,000,000 (ESTIMATE)
ARCHITECT:	Manning Architects | Mackey Mitchel, A Joint Venture
GENERAL CONTRACTOR:	TBD

PROJECT STATUS:

- Design package complete.
- Design-Build package was sent to three (3) General Contractors.
- Bids were received and exceed the $1 million dollar construction budget.
- Revised packages were sent back to contractors to bid the project in two (2) and three (3) phases.
- Revised bids were received, and Campus is currently considering options on moving forward.
- Meeting with Campus scheduled on Tuesday, January 12th, to discuss a path forward.

RIVER PARISHES COMMUNITY COLLEGE

PET PLANT

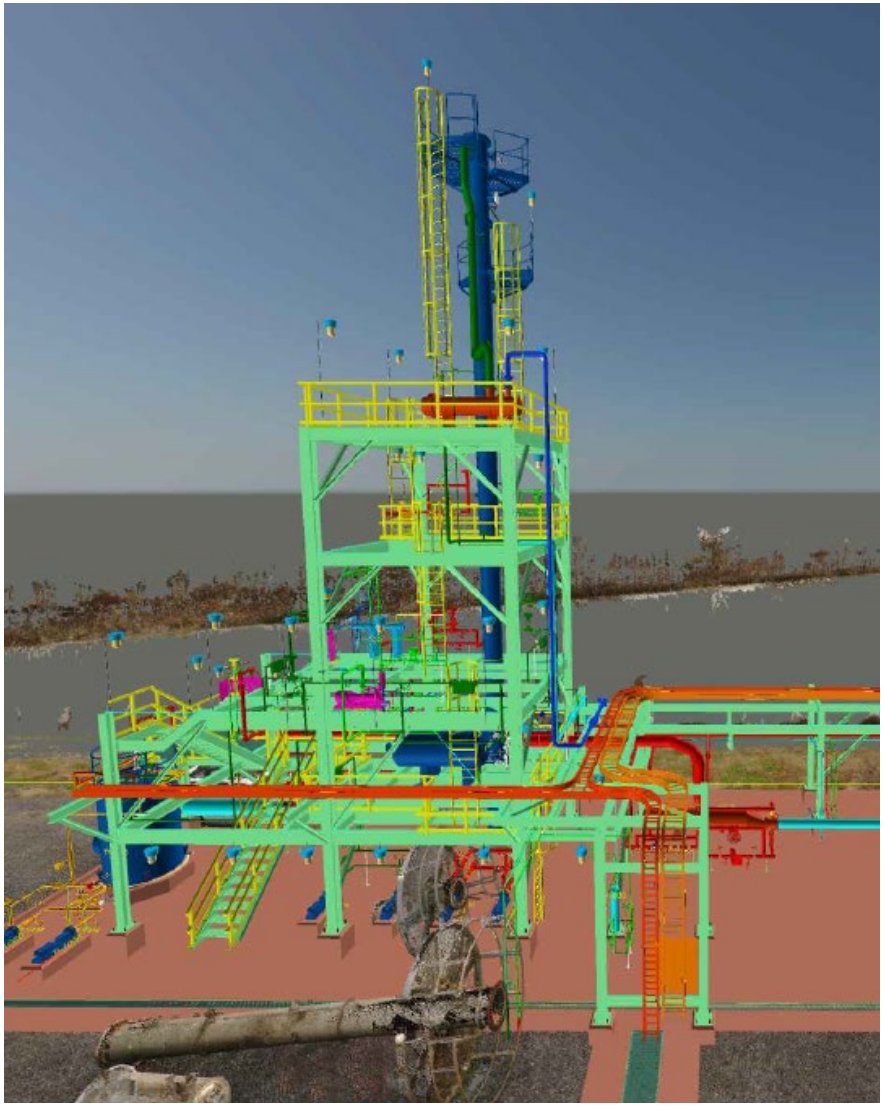

PROJECT:	PET PLANT
LOCATION:	Gonzales
CONSTRUCTION BUDGET:	TBD
DESIGN TEAM:	ISC Constructors, LLC
CONTRACTOR:	TBD

PROJECT STATUS:

- ISC Constructors, LLC has been re-engaged as of meeting on December 2nd, 2020.
- Meeting held on December 16th with ISC; currently working on finishing Design Package.
- Meeting with Campus and ISC scheduled on Wednesday, January 6th, to discuss design status.
- Project to be publicly bid.
- Interested contractors have been contacted.
- Anticipate going to bid March 2022.

LCTCS

END OF UPDATE

January 5, 2020

ACT 391 | ACT 360 I SOWELA DISASTER RECOVERY | OTHER

CSRS | BUILDING STRONGER, SMARTER COMMUNITIES **TOGETHER.**

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

- Baton Rouge Community College, Westside Campus
  - New Building- 21,895 sq. ft.
  - Complete, Occupied January 4, 2013
- Central Louisiana Technical Community College, Shelby Jackson Campus
  - Additions & Renovations- 39,492 sq. ft.
  - Complete, Occupied March 25, 2012
- Central Louisiana Technical Community College, Huey P. Long Campus
  - New Building – 53,448 sq. ft.
  - Complete, Occupied May 18, 2013
- Delgado Community College, Sidney Collier Campus
  - New Building – 39,075 sq. ft.
  - Complete, Occupied July 19, 2013

DCC Sidney Collier

CLTCC Huey P. Long Campus

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

- Delgado Community College, Maritime Training Facility
  - New Building- 19,280 sq. ft.
  - Complete, Occupied April 1, 2016
- Delgado Community College, Learning Resource Center
  - New Building- 14,438 sq. ft.
  - Complete, Occupied June 21, 2014
- Delgado Community College, Delgado (Issac) Hall Mechanical System Upgrades
  - Mechanical System Upgrades – 30,000 sq. ft.
  - Complete, November 18, 2013
- Delgado Community College, Student Services Building Renovation
  - Renovation – 30,450 sq. ft.
  - Complete, Occupied July 14, 2014

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

- Fletcher Technical Community College, Main Campus
  - New Building – 39,075 sq. ft.
  - Complete, Occupied July 7, 2012
- NUNEZ Community College, Arts & Sciences Renovation
  - Project included door repairs, new window blinds, and lighting
  - Complete, Occupied March 18, 2013
- NUNEZ Community College, Allied Health Restoration
  - Project included restoring existing building
  - Roof Project Completed, July 16, 2016
- NUNEZ Community College, Physical Activities Center
  - Additions & Renovations – 2,300 sq. ft.
  - Complete, Occupied February 23, 2016

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

- NUNEZ Community College, Stewart Building
  - New Building – 27,811 sq. ft.
  - Complete, Occupied April 30, 2015
- LCTCS, Student Information System/Disaster Command Center
  - New Building – 16,642 sq. ft.
  - Complete, Occupied June 2016
- Northshore Technical Community College, Florida Parishes Campus
  - New Building- 47,080 sq. ft.
  - Complete, Occupied June 18, 2012
- Northwest Louisiana Technical College, Main Campus
  - New Building- 81,191 sq. ft.
  - Complete, Occupied April 16, 2013

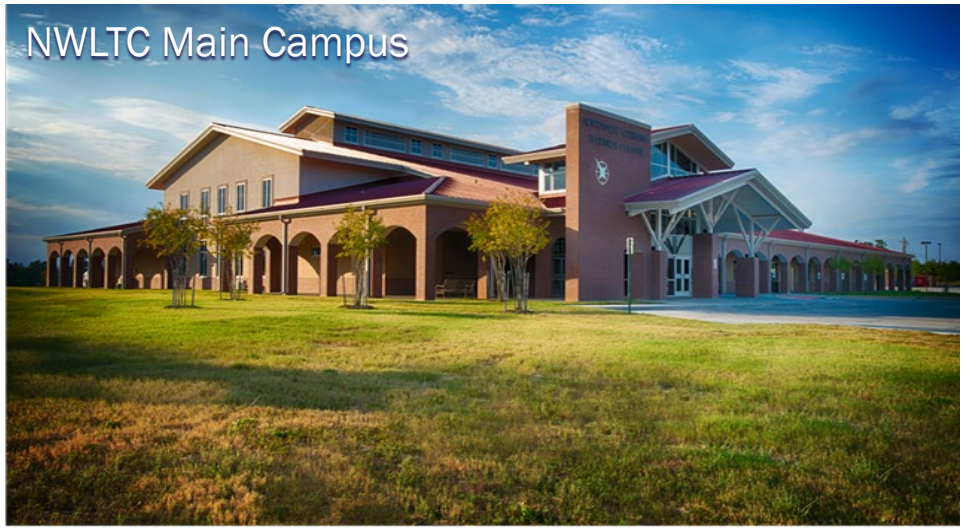

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

- River Parishes Community College, Main Campus
  - New Building – 83,000 sq. ft.
  - Complete, Occupied July 14, 2014
- South Central Louisiana Technical College, Young Memorial Campus
  - New Building Addition and Renovation – 75,572 sq. ft.
  - Complete, Occupied August 20, 2012
- South Louisiana Community College, Gulf Area Campus
  - Renovations – 66,103 sq. ft.
  - Complete, Occupied January 6, 2016
- South Louisiana Community College, Evangeline Campus
  - New Building- 30,000 sq. ft.
  - Complete, Occupied July 2016

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

- SOWELA Technical Community College, Arts & Sciences Building
  - New Building – 45,752 sq. ft.
  - Complete, Occupied March 2, 2012

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

LCTCS ACT 391 PROGRAM

COMPLETED PROJECTS

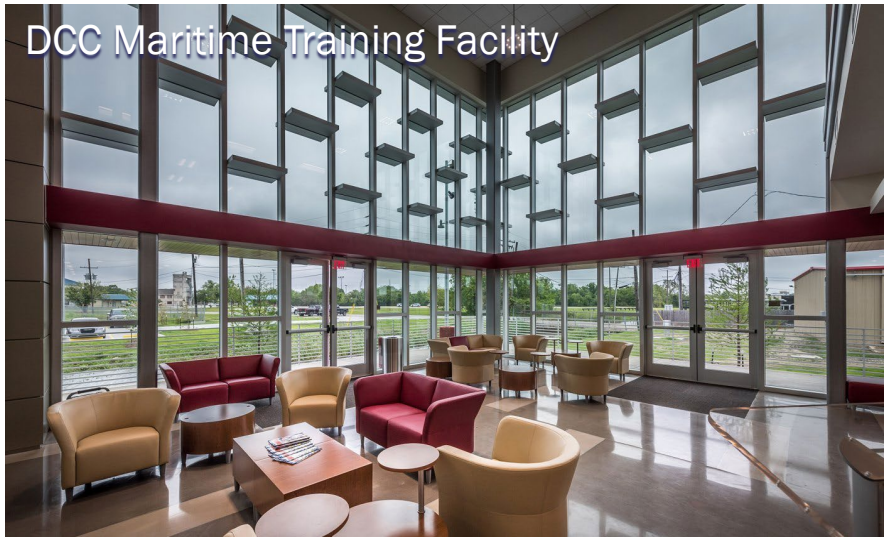

LCTCS ACT 360 PROGRAM

COMPLETED PROJECTS

- Baton Rouge Community College, Central Campus
  - Renovations– 19,000 sq. ft.
  - Complete, Occupied September 15, 2015
- Baton Rouge Community College, Ardendale Campus
  - New Building– 25,924 sq. ft.
  - Complete, Occupied May 15, 2018
- Baton Rouge Community College, Acadian Campus
  - Renovations– 130,000 sq. ft.
  - Complete, Occupied September 24, 2019
- Bossier Parish Community College, STEM Building
  - New Building – 80,000 sq. ft.
  - Complete, Occupied May 23, 2017

LCTCS ACT 360 PROGRAM

COMPLETED PROJECTS

- Central Louisiana Technical Community College, Alexandria Downtown Campus
  - New Building – 50,000 sq. ft.
  - Complete, Occupied September 6, 2019
- Central Louisiana Technical Community College, Alexandria Riverfront Campus
  - Renovation – 23,000 sq. ft.
  - Complete, Occupied August 2, 2019
- Delgado Community College, River City Campus
  - New Building – 74,638 sq. ft.
  - Complete, Occupied July 12, 2018
- Louisiana Delta Community College, Jonesboro Campus
  - Renovations – 21,000 sq. ft.
  - Complete, Occupied January 4, 2016

LCTCS ACT 360 PROGRAM

COMPLETED PROJECTS

- Louisiana Delta Community College, Monroe Campus
  - New Building & Renovations – 22,000 sq. ft.
  - Complete, Occupied September 12, 2019
- Louisiana Delta Community College, Tallulah Campus
  - New Building & Renovations – 42,479 sq. ft.
  - Complete, Occupied August 27, 2019
- Louisiana Delta Community College, Winnsboro Campus
  - Renovations – 35,000 sq. ft.
  - Complete, Occupied February 10, 2017
- Northshore Technical Community College, STEM Center Building
  - New Building – 33,000 sq. ft.
  - Complete, Occupied January 20, 2017

LCTCS ACT 360 PROGRAM

COMPLETED PROJECTS

- Northshore Technical Community College, Livingston Campus
  - New Building – 14,000 sq. ft.
  - Complete, Occupied August 7, 2019
- Northwest Louisiana Technical Community College, Workforce Development Building
  - Addition – 6,832 sq. ft.
  - Complete, Occupied September 26, 2016
- River Parish Community College, Technical Training Center
  - New Building – 39,973 sq. ft.
  - Complete, Occupied January 9, 2017
- River Parish Community College (SCLTC), Reserve Campus
  - New Building – 26,587 sq. ft.
  - Complete, Occupied January 21, 2017

LCTCS ACT 360 PROGRAM

COMPLETED PROJECTS

- South Louisiana Community College (SCLTC), Young Memorial Campus
  - New Building – 10,442 sq. ft.
  - Complete, Occupied November 28, 2016
- South Louisiana Community College, Allied Health Building
  - New Building – 61,524 sq. ft.
  - Complete, Occupied December 7, 2016
- SOWELA Technical Community College, Student Services Building
  - New Building – 23,000 sq. ft.
  - Complete, Occupied November 13, 2017

LCTCS ACT 360 PROGRAM

COMPLETED PROJECTS

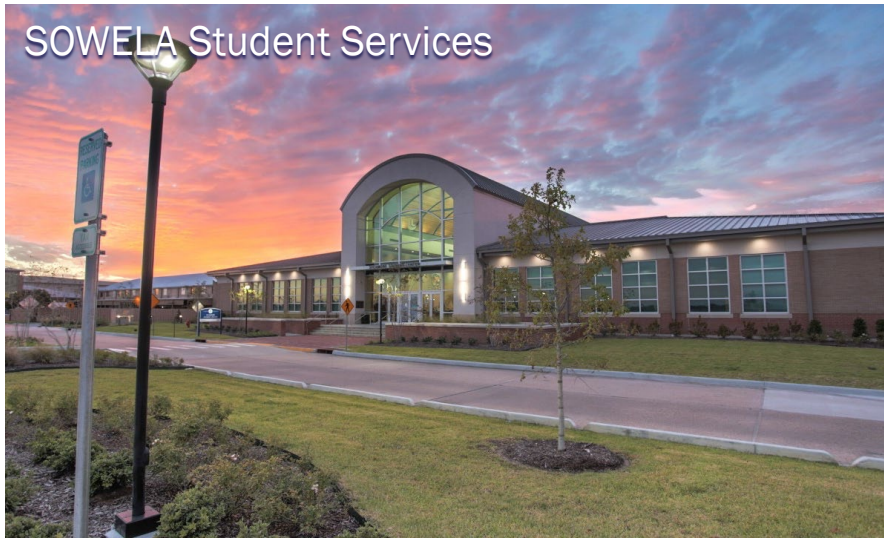

LCTCS ACT 360 PROGRAM

COMPLETED PROJECTS
